



Southeast Infrastructure Improvements (Garfield to Beach and 3rd to 7th)

Project Information:


Completion Date
November 2020

Project Team
DGR Engineering is performing the construction administration services for the project. Please contact the following project team members below with any questions or concerns.

DGR Engineering
Riley Rinehart, El
Project Engineer
Riley.Rinehart@dgr.com
Office: (605) 339-4157


City of Dell Rapids
Justin Weiland
City Administrator
Cityadmin@cityofdellrapids.com
Office: (605) 428-3595

H&W Contracting, LLC
John Rennich
Superintendent of Construction
estimator@h-wcontracting.com
Office: (605) 339-8834
Cell: (605) 595-8595

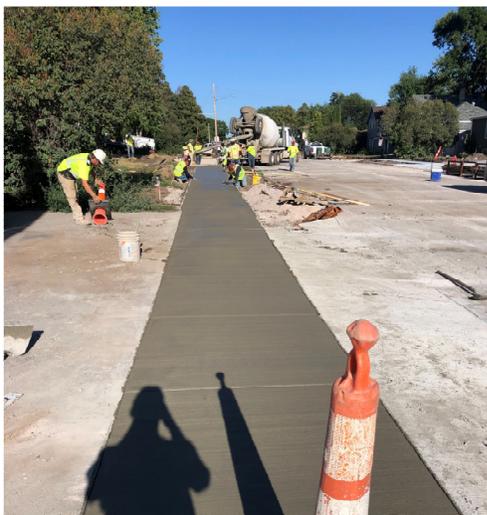

Project Overview:

This project consists of drainage, sanitary sewer, and water main improvements, along with major street improvements. Construction will generally take place in the area from Garfield Avenue to Beach Avenue and from 3rd Street to 7th Street, excluding 6th Street. Work began in August 2019 and the project is expected to be complete in November 2020.

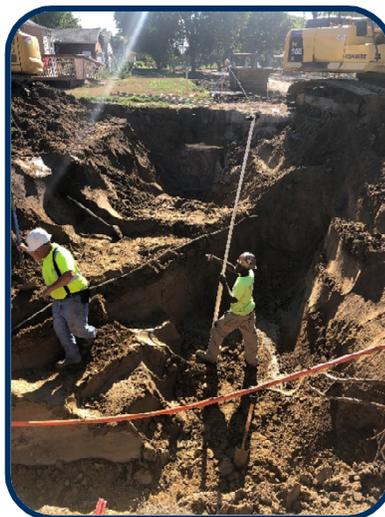

Work Completed:

- Sidewalks and driveways were installed along 7th Street between Garfield Avenue and Beach Avenue.
- Water main and water service lines were installed through the alley north of 4th Street between Washington Avenue and Beach Avenue.
- Water main was installed along Beach Avenue and 4th Street. Water service lines were directional drilled into the backyards for the properties along the south side of 4th Street.
- Sanitary sewer installation began on Beach Ave.
- The base course was fine graded to prepare for asphalt on 5th Street, Washington Avenue, Dakota Avenue, and Vermont Avenue.

Upcoming Work:

The Contractor will finish installing sidewalks and driveways along 7th Street, 5th Street, and Washington Avenue. The water main connection at the intersection of 4th Street and Garfield Avenue will be completed and the concrete pavement will be replaced. The Contractor will finish installing the water services, sanitary sewer, and storm sewer along 4th Street. It is anticipated that the water service connections in the backyards of the properties along the south side of 4th Street will be completed next week or the week of September 14.

The Contractor will finish installing the sanitary sewer along Beach Avenue and through the alley north of 4th Street between Washington Avenue and Beach Avenue. They will also begin blasting bedrock and installing the utilities along 7th Street between Beach Avenue and the railroad tracks. The blasting is expected to be completed next week and temporary water lines will need to be installed in advance.

Construction progress meetings are held at 10:00 a.m. on the first and third Tuesdays of the month. The next meeting will be held near the intersection of 3rd Street and Washington Avenue on Tuesday, September 15th. The public is invited to attend.

The City is using a text messaging system to send out updates on street closures, planned water service disruptions, etc. throughout construction of the project. To subscribe to the text message updates, text the word "PROJECT" to 605-206-2927.

